


# SCICLONE<sup>®</sup> SEPARATOR

## Concrete Installation Manual




Play Setup Video

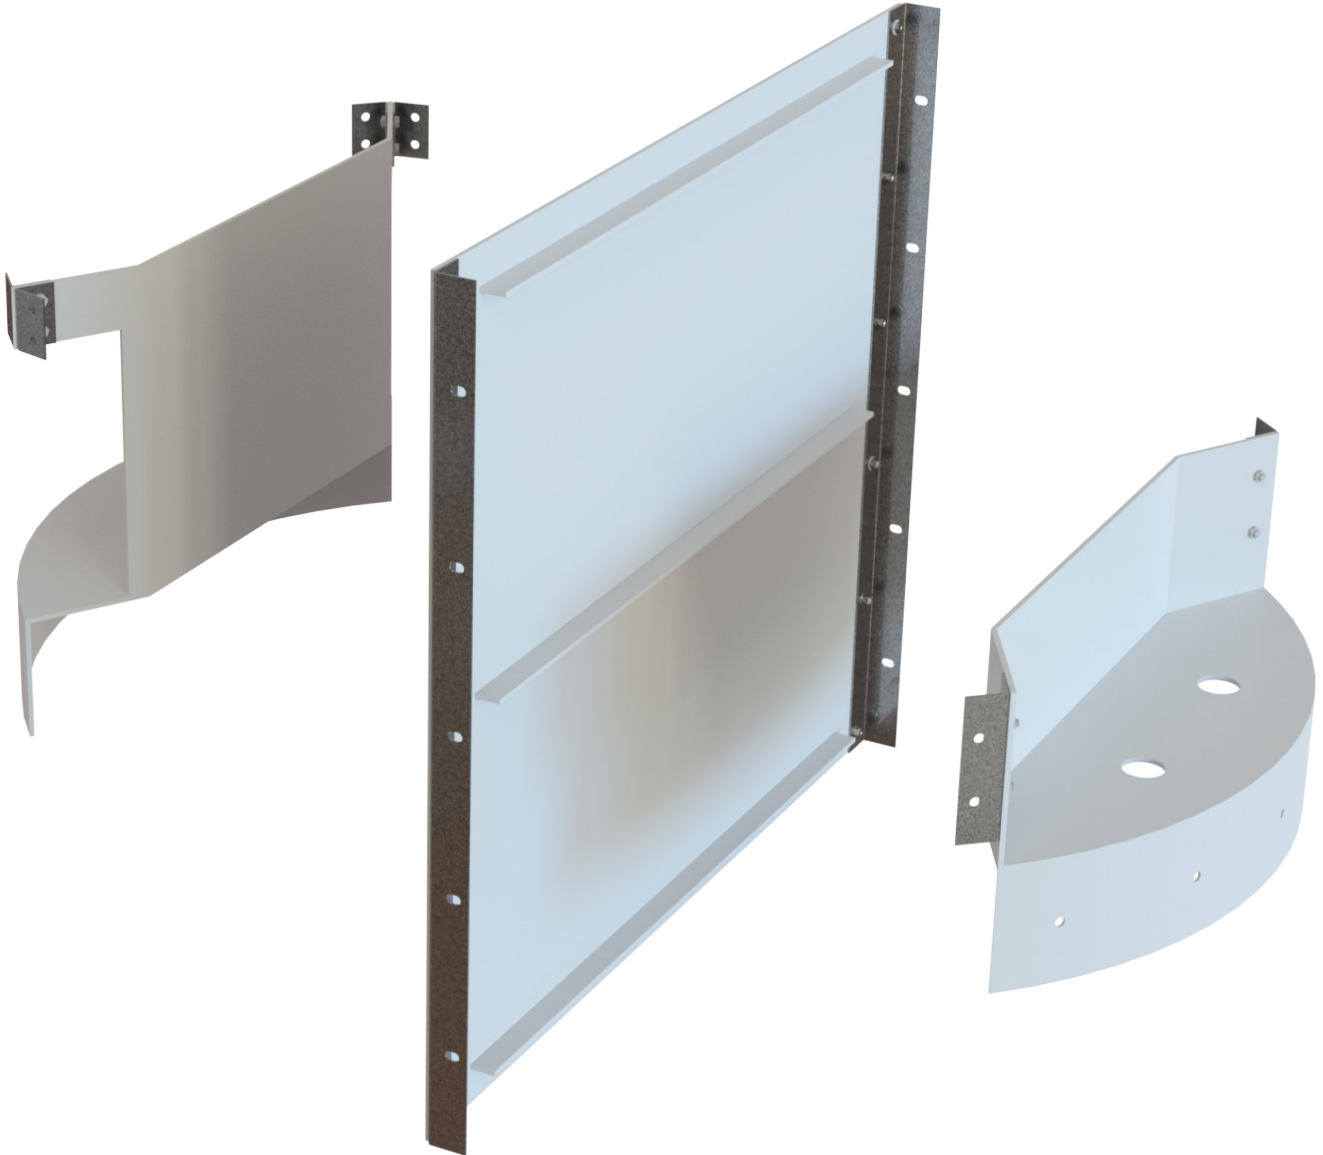

English

# OVERVIEW

The SciClone® Separator is designed to remove high levels of trash, debris, sediments and hydrocarbons. Its simple design allows for quick and easy installation. The system is housed in a standard precast manhole structure and can be installed at various depths to meet site-specific conditions. Various size units are available from 4' to 12' in diameter. In some areas, 13' and 14' diameter units may be available.

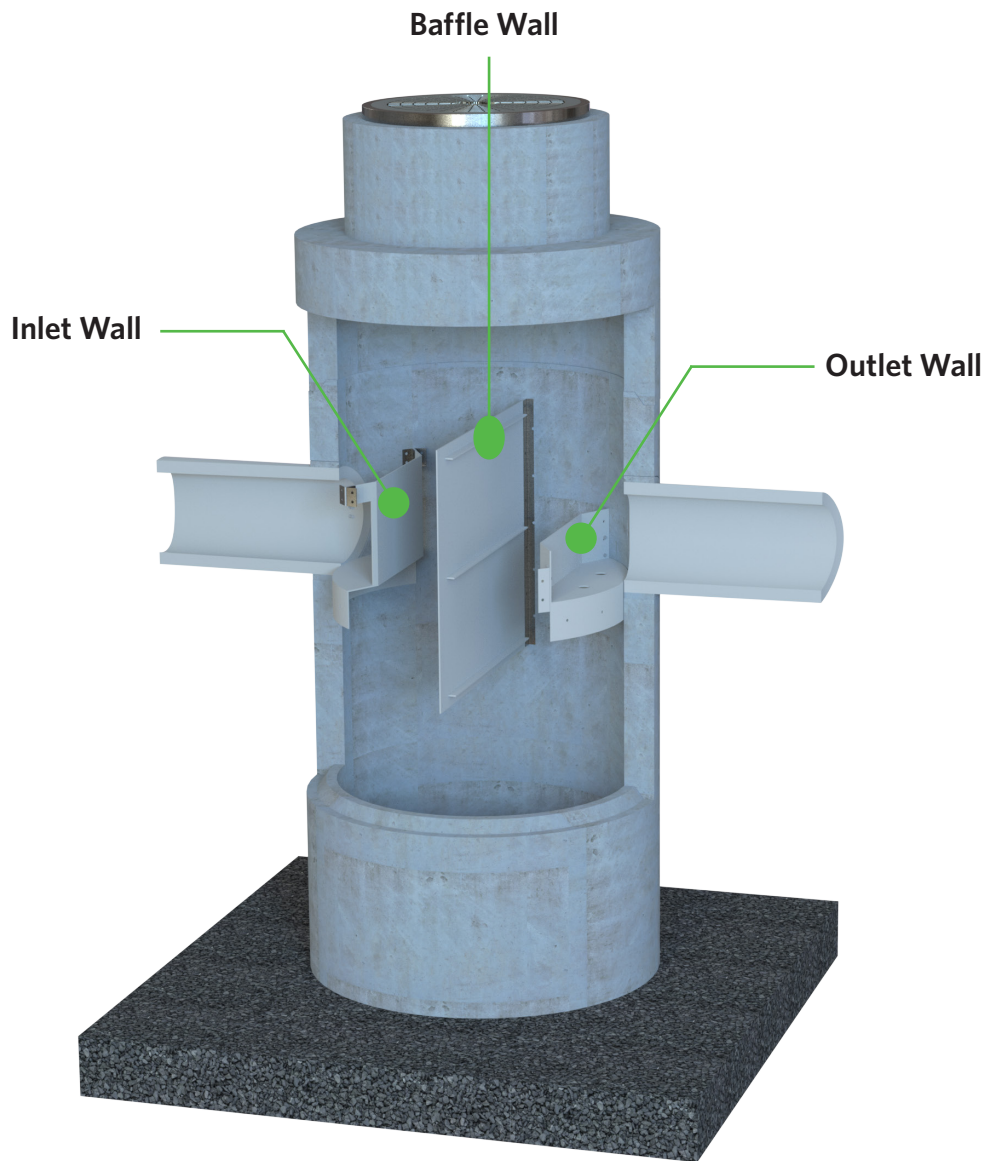

## INTRODUCTION

This is the Bio Clean SciClone® Separator installation manual. Before starting, make sure that there is enough room for installing and assembling the product. Inspect all materials for defects and gather the recommended tools listed on the following page. The contractor shall furnish all labor, equipment, materials, and incidentals required to install the SciClone® Separator and appurtenances in accordance with the contract documents. Any damage to the existing drainage structure (retrofit applications) or surrounding infrastructure that may need to be repaired to allow for proper installation of the SciClone shall be considered incidental and to be paid for at no cost to the client. Bio Clean offers installation services in certain areas. Please contact Bio Clean for more information on pre-authorized third party contractors who can provide installation services in your area.

# INSTRUCTIONS

## DELIVERY & UNLOADING/LIFTING

- Bio Clean Environmental Services, Inc. shall deliver the unit(s) to the site in coordination with the Contractor.
- The Contractor may be required to provide spreader bars and chains/cables to safely and securely lift the base section, risers, and top section along with suitable lifting hooks, knuckles, shackles and eyebolts.
- Please see project specific drawings for weights and lifting details. Contact Bio Clean for additional lifting details. Internal components are pre-installed prior to delivery.


## INSPECTION

Inspection of the SciClone® Separator and all parts contained in or shipped outside of the unit shall be inspected at time of delivery by the site Engineer/Inspector and the Contractor. Any nonconformance to approved drawings or damage to any part of the system shall be documented on the Bio Clean shipping ticket.

- Damage to the unit during and after unloading shall be corrected at the expense of the Contractor. Any necessary repairs to the SciClone® Separator unit shall be made to the acceptance of the Engineer/Inspector.

## SITE PREPARATION

- The Contractor is responsible for providing adequate and complete vault protection when the SciClone® Separator unit is installed prior to final site stabilization (full landscaping, grass cover, final paving, and street sweeping completed).
- The Contractor shall adhere to all jurisdictional and/or OSHA safety rules in providing temporary shoring of the excavation.
- The Contractor or Owner is responsible for appropriately barricading the SciClone® Separator unit from traffic (in accordance with local codes).



- Each SciClone® Separator unit shall be constructed based on the locations and elevations according to the sizes shown on the approved drawings. Any modifications to the elevation or location shall be at the direction of and approved by the Engineer.
- The SciClone® Separator unit shall be placed on level compacted sub-grade with a minimum 6-inch gravel base. Compact undisturbed sub-grade materials to be per Geotechnical/Soils report. Unsuitable material below sub-grade shall be replaced to site engineer's approval. Place granular sub-base and compact to State and local standards as per the Engineers requirements.
- Once the base piece is set, the riser(s) and top section should be sealed onto the base section before backfilling, using a non-shrink grout, butyl rubber or similar waterproof seal.
- Pipe connections shall be aligned and sealed to meet the approved drawings with modifications necessary to meet site conditions and local regulations. The correct connection (inlet/outlet) will be marked on the Bio Clean Vault unit. NOTE: The inlet and outlet pipe cannot protrude past the structures I.D. wall as it will interfere with the internal components.

# INSTRUCTIONS

- Once the SciClone® Separator unit is set, it should be protected from construction runoff entering it. Contractor will be responsible for cleaning if unit is contaminated by such construction runoff and associated pollutants and damaged (i.e. concrete wash water).
- Backfilling should be performed in a careful manner, bringing the appropriate fill material up in 6-inch lifts on all sides. Precast sections shall be set in a manner that will result in a watertight joint. In all instances, installation of the SciClone® Separator unit shall conform to ASTM specification C891 "Standard Practice for Installation of Underground Precast Utility Structures" unless specified otherwise in contract documents.
- If applicable, it is the responsibility of the Contractor to provide curb and gutter and transition to the SciClone® Separator unit for proper stormwater flow into the system through the throat, pipe or grate opening. A standard drawing of the throat and gutter detail is available in the following section; however the plans and contract documents supersede all standard drawings. Several variations of the standard design are available. Effective bypass for an offline SciClone® Separator unit is essential for correct operation (i.e. bypass to an overflow at lower elevation).

## INSTALLATION

1. The SciClone® Separator unit shall be placed on level compacted sub-grade with a minimum 6-inch gravel base and mark the base. Compact undisturbed sub-grade materials to be per Geotechnical/ Soils report. Unsuitable material below sub-grade shall be replaced to site engineer's approval. Place granular sub-base and compact to State and local standards as per the Engineers requirements.




Set the base section of the SciClone™ on solid sub-grade using appropriate rigging and lifting method. There are mounting locations around the concrete structure.

# INSTALLATION


2.

After placing the base structure, add watertight seal (either mastic rope or rubber gasket). Verify the level and elevation of the base section before adding any additional precast riser sections.

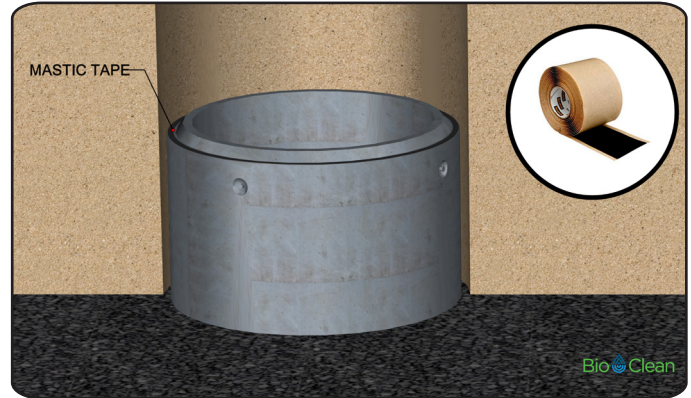


3.

Set riser section(s) on the base section. Set the riser section that contains the S Sci-Clone® Separator components. Verify the inlet and outlet pipe elevation using precise survey methods. Be sure to add watertight seal to each rise section.

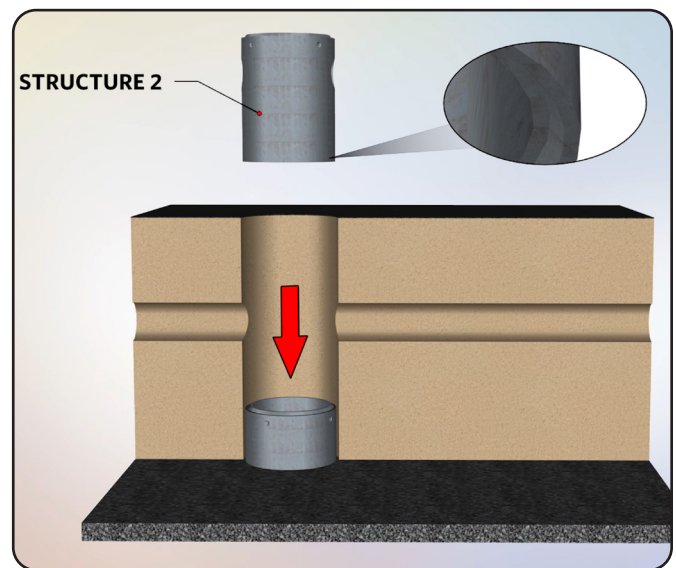

5.


Set any additional riser sections, if required, using the same method as previous section. Be sure to add watertight seal to each rise section.

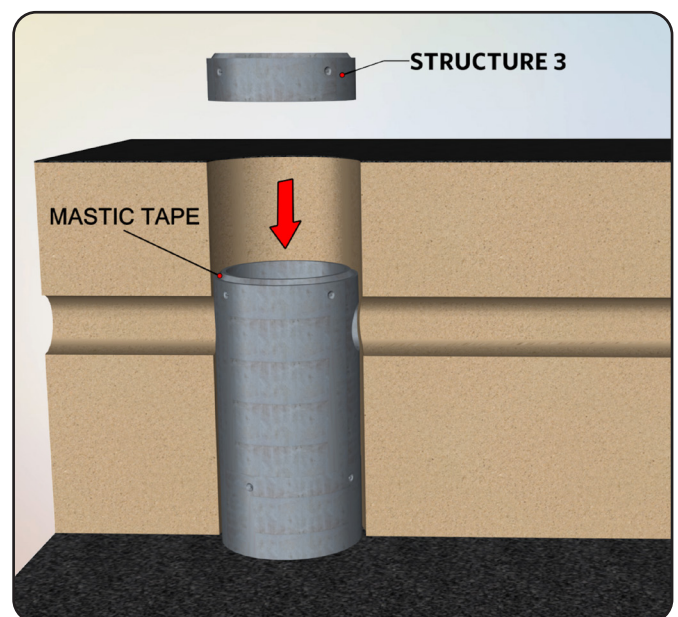




## INSTALLATION

6.

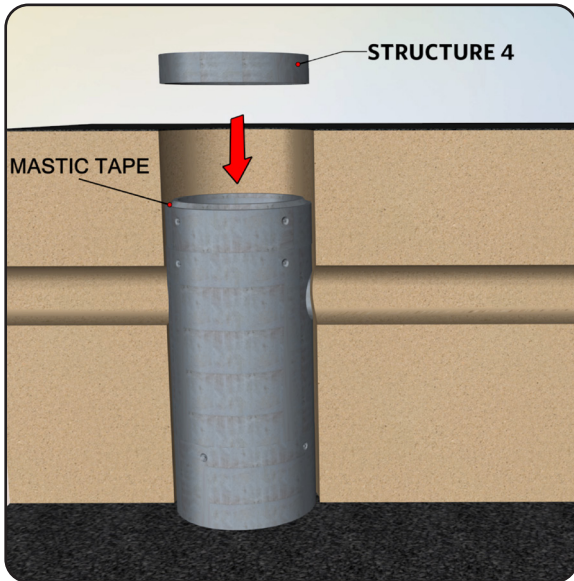


Set the top slab. Note the top slab's orientation. The maintenance hole access opening(s) must be oriented over the inlet and outlet side of the oil/floatables skimmer per the drawings.

7.

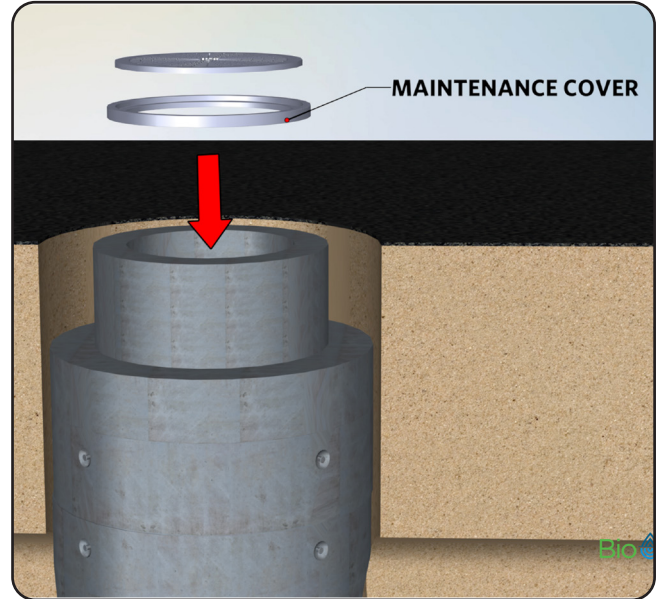

Set the access risers (if applicable) to bring the Maintenance hole frame and covers up to finish surface elevation per the approved drawings and plans. Set manhole covers over the top of the access risers. Use grout to adjust manhole frames to the proper elevations.

## PIPE CONNECTIONS

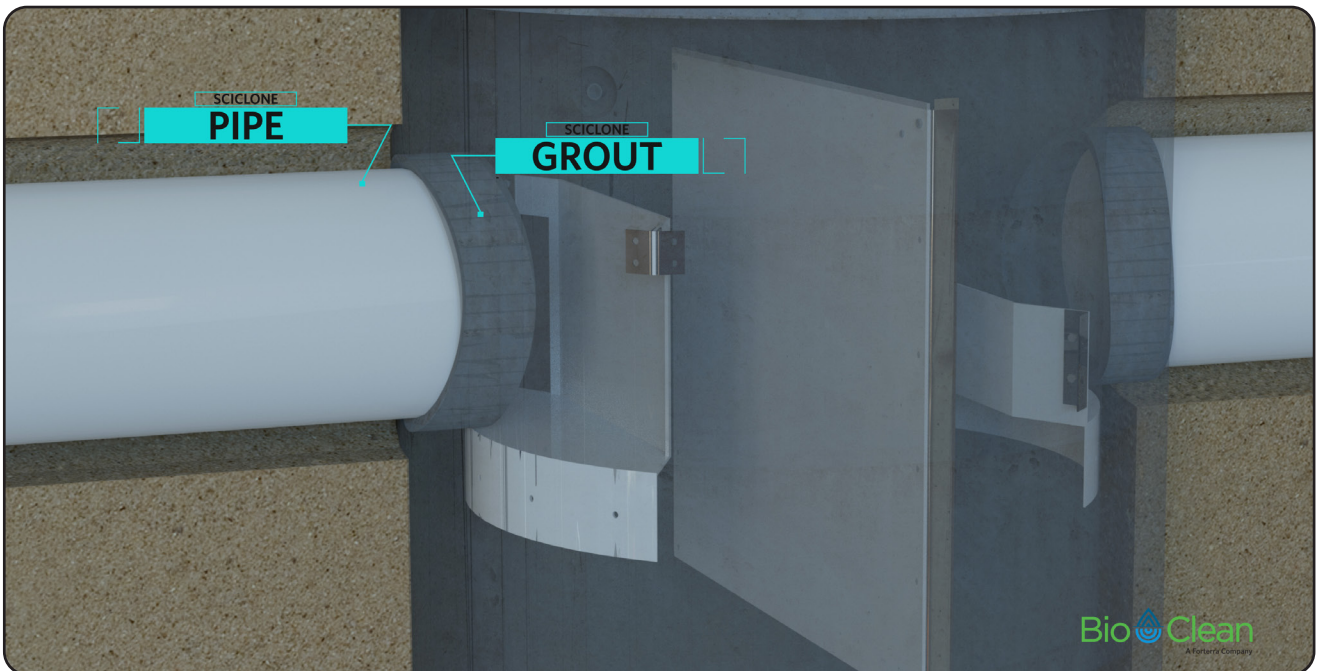

Inlet pipe(s) shall be stubbed in and connected to the precast manhole according to the Engineer's requirement or specifications. The Contractor is to grout all inlet pipes flush with the interior wall of the structure per plans and specifications.

## PIPE CONNECTIONS

- Outlet pipe shall be stubbed in and connected to the precast manhole according to the Engineer's requirement or specifications. The Contractor is to grout all inlet pipes flush with the interior wall of the structure per plans and specifications.
- It is pivotal that installation of the pipe is well centered and in the appropriate position along with ensuring the grout is clean and properly finished. Re-excavate and reconnect the pipe properly as needed to ensure proper installation. Once the pipes are connected, carefully backfill around them, compacting in "lifts" that will not deflect, disturb or damage them.

### BAD EXAMPLE OF A PIPE INSTALLATION




Example of a BAD pipe installation. Protruding past the internal wall of the structure, poor grouting, and wrong position.



Example of a GOOD pipe installation. Pipe flush with the internal wall of the structure, clean grouting, and proper position.

## TECHNICAL SUPPORT

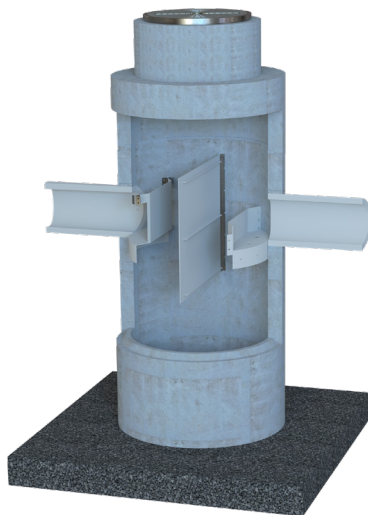

**Contech Engineered Solutions**  
**9100 Centre Pointe Drive**  
**West Chester, OH 45069**

<https://www.conteches.com/technical-guides/>

**Contact Us:**  
**Phone: 1-800-338-1122**  
**Email: [Info@Conteches.com](mailto:Info@Conteches.com)**
